PROJECT SCOPE / P6 LIVE CLASS

Garden Seating Area

Project ID: GSA-001

Fictional training project | 4 activities

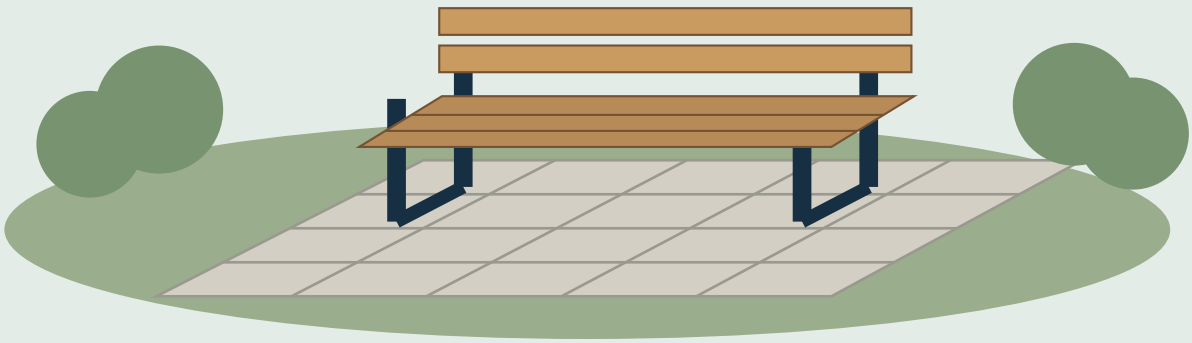

Illustrative sketch, not to scale.

Scope

Create a small paved seating area with one timber bench. Prepare the area, lay dry-laid paving, assemble the bench, then position it and inspect the finished work.

Activities to enter in Primavera P6

Activity ID	Activity name	Duration	Predecessor(s)
A100	Clear and prepare area	1 day	None
A200	Lay dry-laid paving	3 days	A100
A300	Assemble timber bench	2 days	A100
A400	Position bench and inspect	1 day	A200, A300

Scheduling assumptions

All links are Finish-to-Start (FS), with zero lag. After A100, separate crews can perform A200 and A300 in parallel. A400 waits for both to finish.

Use one Monday-Friday calendar, 8 hours/day, no holidays. All four activities are Task Dependent. Use the tutor-selected project start and matching Data Date; no constraints or resource leveling.

Class task: Create the project, enter the four activities and relationships, then schedule. Identify the project duration, critical path and Total Float.
